


## TIMELINE

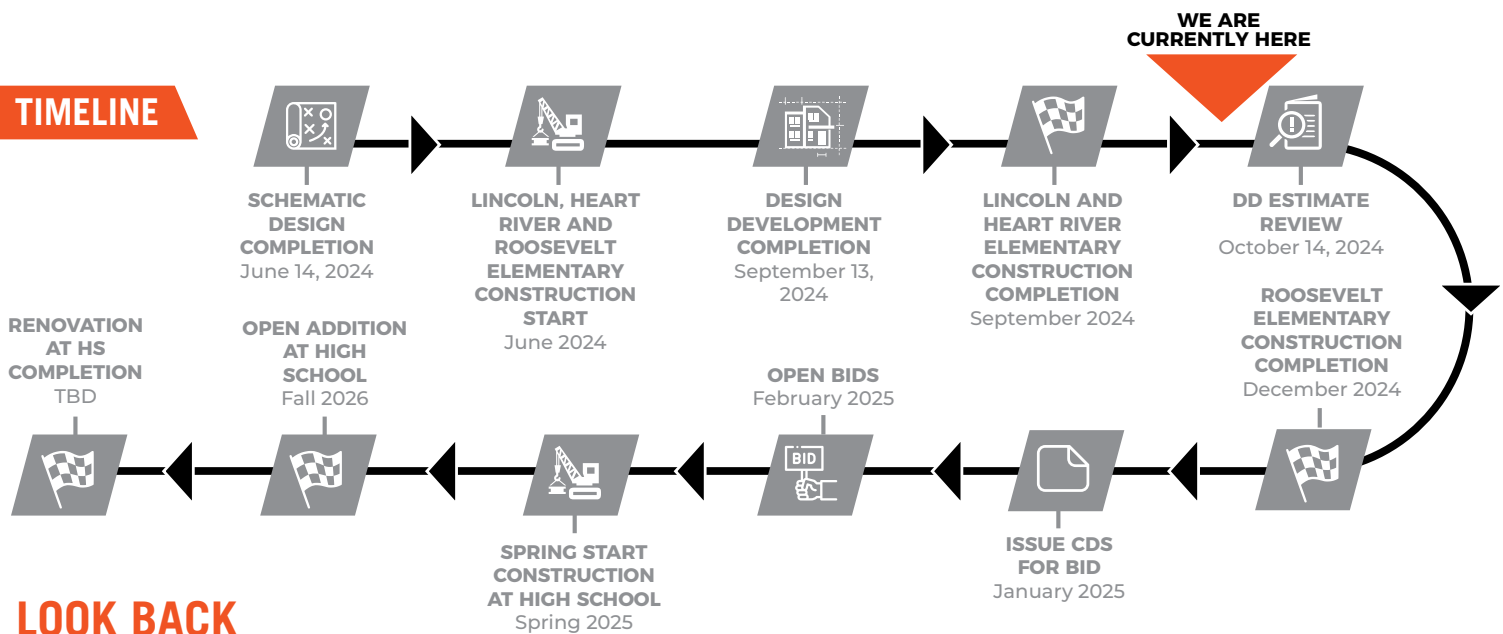

## LOOK BACK

- **October 24th:** Successful bond vote 70% approval
- **December 19th:** JE Dunn selected as CMaR
- **November - September:** 12 Executive Design Committee meetings
- **September-August:** Over 30 meetings with teacher input groups
- **June 14th:** Completion of Schematic Design at the HS
- Seven meetings with city officials
- **August 12th:** Heart River and Lincoln Elementary schools moved into their new spaces
- **September 13th:** DD drawing package completed

## LOOK FORWARD

- **October:** DD estimate review with J.E. Dunn
- **October 17th & 18th:** Hazardous material investigation
- **October:** planned removal of site irrigation well
- **October:** Grant application for whole building backup generation submitted





Concept interior rendering of student commons

## DICKINSON HIGH SCHOOL PROJECT HIGHLIGHTS

- Approx. 81,000 sf of demolition
- Approx 88,000 sf of existing building with approx 22,000 sf of remaining building renovation
- Approx 104,000 sf of new construction
- Space for 1,400 students
- 8 science labs
- 28 educational space
- Student commons/ lunchroom
- 600 Capacity theater with alternates
- Natural light for all new student spaces

