




TIMELINE

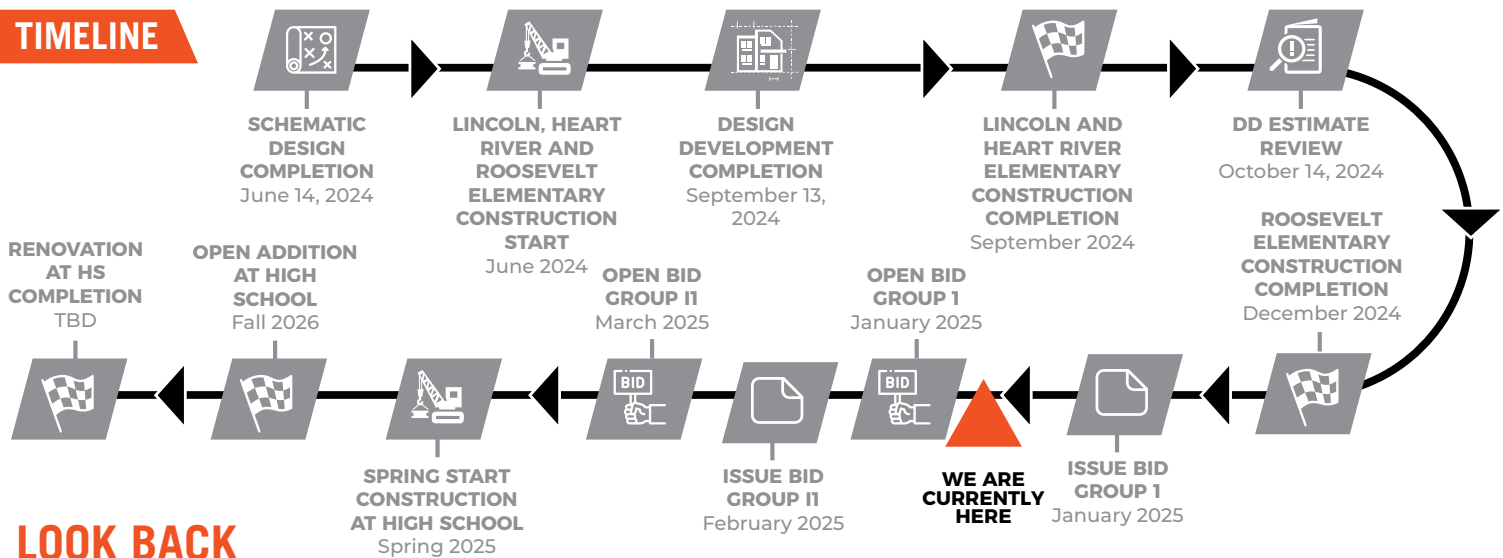

LOOK BACK

- **October 24th:** Successful bond vote 70% approval
- **December 19th:** JE Dunn selected as CMaR
- **November - September:** 12 Executive Design Committee meetings
- **September-August:** Over 30 meetings with teacher input groups
- Eight meetings with city officials
- **August 12th:** Heart River and Lincoln Elementary schools moved into their new spaces
- **January 8th:** First advertisement for bidding of Bid Group I

LOOK FORWARD

- **January:** Apply for state water grant
- **January 16th:** Full drawings set page turn and final finish review
- **January 30th:** Bid Group I bid opening
- **February:** Bid Group II bid release
- **March:** Bid Group II bid opening
- **March:** Furniture package user group meetings



Interior Renderings



DICKINSON HIGH SCHOOL PROJECT HIGHLIGHTS

- Approx. 81,000 sf of demolition
- Approx 88,000 sf of existing building with approx 22,000 sf of remaining building renovation
- Approx 104,000 sf of new construction
- Space for 1,400 students
- 7 science labs
- 35 educational spaces in addition
- Student commons/ lunchroom and media center
- 600 Capacity theater with alternates
- Natural light for all new student spaces

Exterior Rendering



SCAN ME
