


TIMELINE

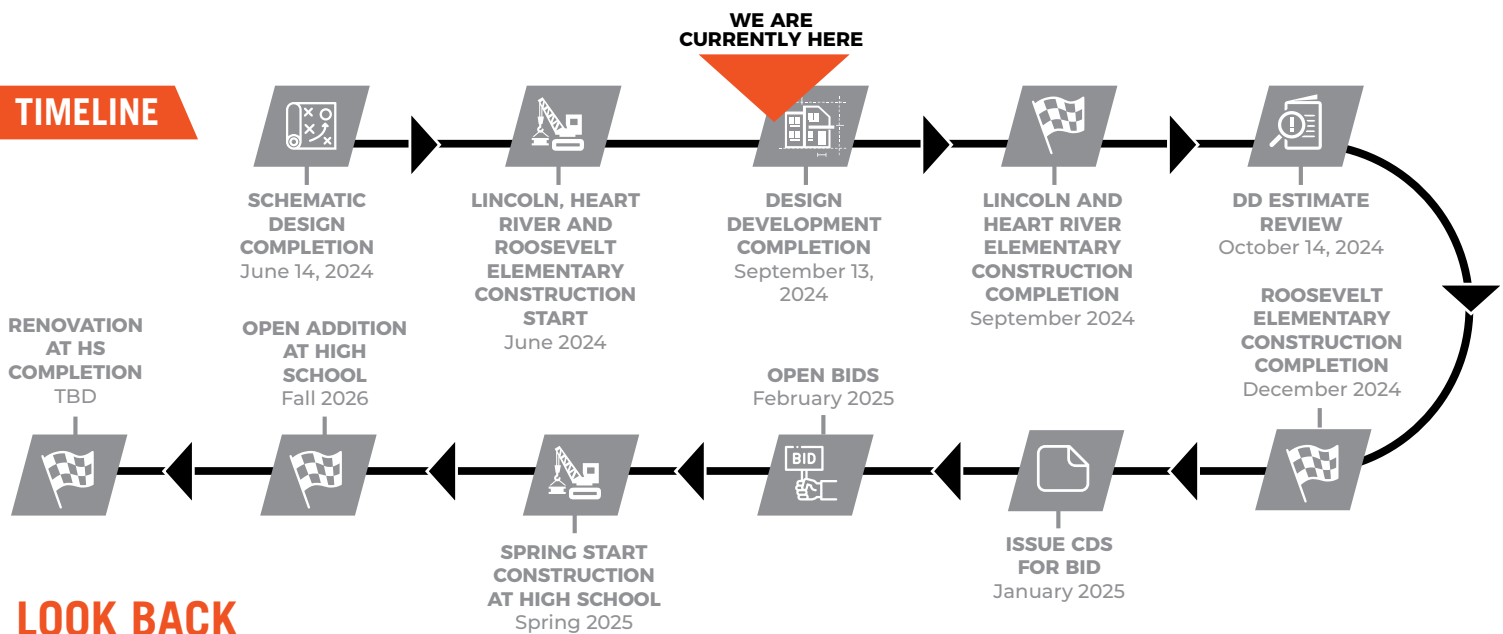

LOOK BACK

- **October 24th:** Successful bond vote 70% approval
- **November:** Completed eight case studies tours at other High Schools in ND
- **December 19th:** JE Dunn selected as CMaR
- **November - September:** 12 Executive Design Committee meetings
- **September-August:** Over 30 meetings with teacher input groups
- **June 14th:** Completion of Schematic Design at the HS
- Six meetings with city officials
- **August 12th:** Heart River and Lincoln Elementary schools moved into their new spaces

LOOK FORWARD

- **Week of September 9th:** Planned underground utilities investigation
- **October:** Planned Soil borings completed
- **September 13th:** DD drawing package completed
- **October:** DD estimate review with J.E. Dunn





Roosevelt Elementary Addition - Construction Progress Photo

DICKINSON HIGH SCHOOL PROJECT HIGHLIGHTS

- Approx. 81,000 sf of demolition
- Approx 88,000 sf of existing building with approx 22,000 sf of remaining building renovation
- Approx 104,000 sf of new construction
- Space for 1,400 students
- 8 science labs
- 28 educational space
- Student commons/ lunchroom
- 600 Capacity theater
- Natural light for all new student spaces

